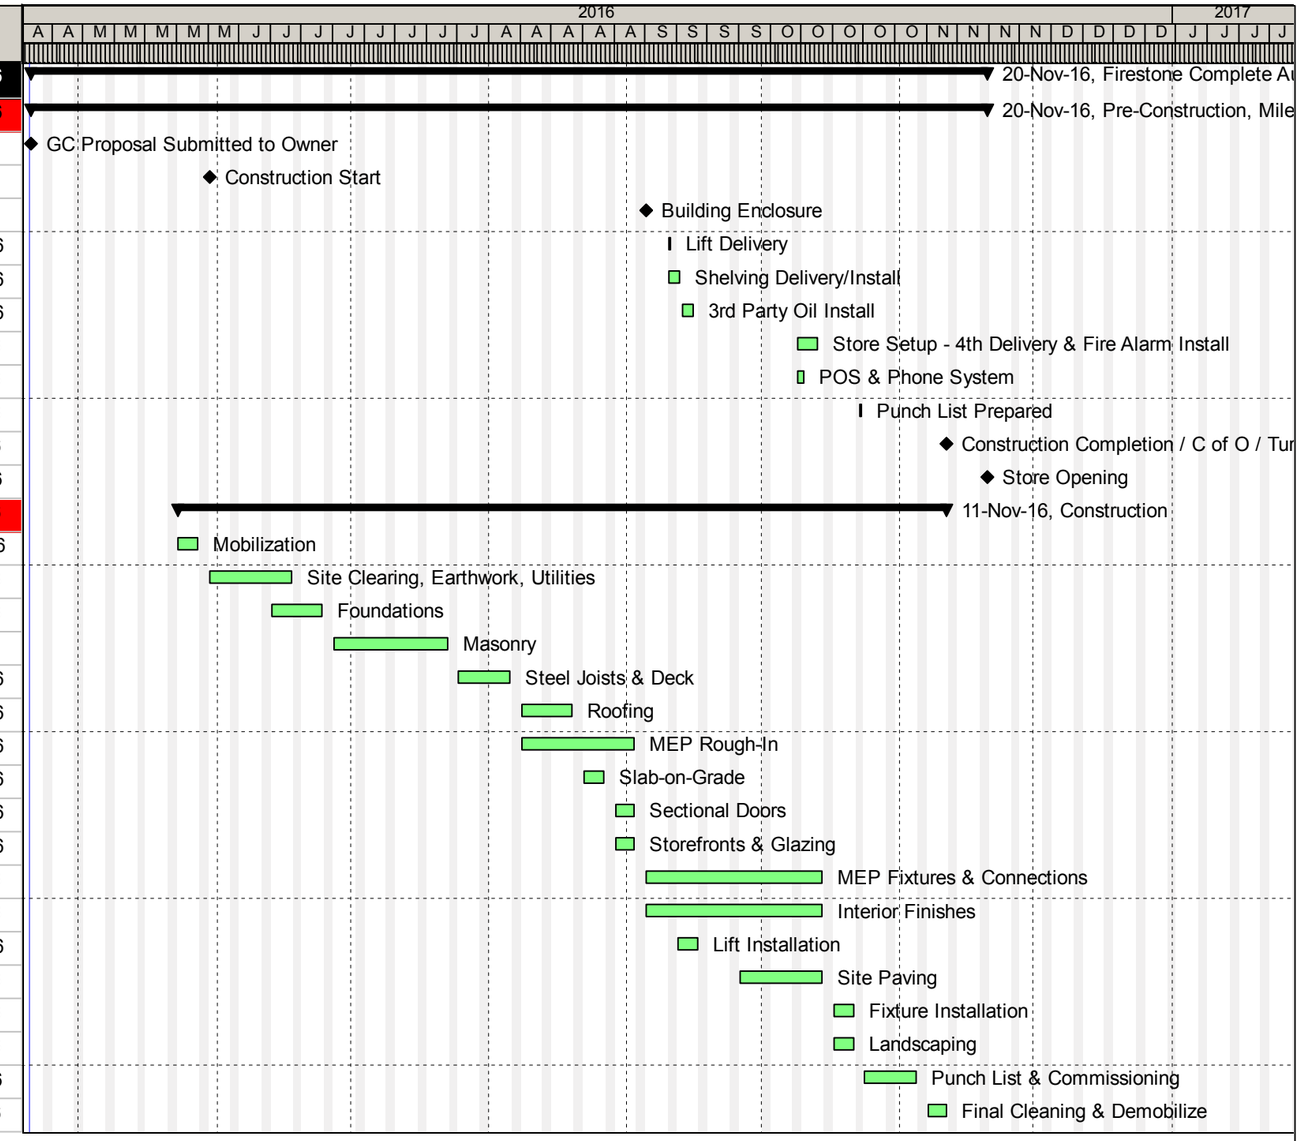Activity ID	Activity Name	Duration	Tentative Start	Tentative Finish
Firestone Complete Auto Care (Mentor, OH)		153	20-Apr-16	20-Nov-16
Pre-Construction, Milestones, & OFE		153	20-Apr-16	20-Nov-16
A1000	GC Proposal Submitted to Owner	0	20-Apr-16	
A1010	Construction Start	0	30-May-16	
A1160	Building Enclosure	0	05-Sep-16	
A1020	Lift Delivery	1	10-Sep-16	10-Sep-16
A1030	Shelving Delivery/Install	2	10-Sep-16	12-Sep-16
A1040	3rd Party Oil Install	3	13-Sep-16	15-Sep-16
A1050	Store Setup - 4th Delivery & Fire Alarm Install	5	09-Oct-16	13-Oct-16
A1060	POS & Phone System	2	09-Oct-16	10-Oct-16
A1070	Punch List Prepared	1	23-Oct-16	23-Oct-16
A1080	Construction Completion / C of O / Turnover	0		11-Nov-16
A1090	Store Opening	0		20-Nov-16
Construction		125	23-May-16	11-Nov-16
A1110	Mobilization	5	23-May-16	27-May-16
A1100	Site Clearing, Earthwork, Utilities	15	30-May-16	17-Jun-16
A1120	Foundations	10	13-Jun-16	24-Jun-16
A1130	Masonry	20	27-Jun-16	22-Jul-16
A1140	Steel Joists & Deck	10	25-Jul-16	05-Aug-16
A1150	Roofing	10	08-Aug-16	19-Aug-16
A1200	MEP Rough-In	20	08-Aug-16	02-Sep-16
A1190	Slab-on-Grade	5	22-Aug-16	26-Aug-16
A1170	Sectional Doors	5	29-Aug-16	02-Sep-16
A1180	Storefronts & Glazing	5	29-Aug-16	02-Sep-16
A1230	MEP Fixtures & Connections	30	05-Sep-16	14-Oct-16
A1240	Interior Finishes	30	05-Sep-16	14-Oct-16
A1220	Lift Installation	5	12-Sep-16	16-Sep-16
A1250	Site Paving	15	26-Sep-16	14-Oct-16
A1210	Fixture Installation	5	17-Oct-16	21-Oct-16
A1260	Landscaping	5	17-Oct-16	21-Oct-16
A1270	Punch List & Commissioning	10	24-Oct-16	04-Nov-16
A1280	Final Cleaning & Demobilize	5	07-Nov-16	11-Nov-16
