

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	31 May '20							07 Jun '20							14 Jun '20	
					S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M			
1			POM+Project	135 days	Tue 02/06/20	Mon 07/12/20																	
2			R&D product development	65 days	Tue 02/06/20	Mon 31/08/20																	
3			Need survey	20 days	Tue 02/06/20	Mon 29/06/20																	
4			Set product spec	15 days	Tue 30/06/20	Mon 20/07/23																	
5			Shelf life report	10 days	Tue 21/07/20	Mon 03/08/24																	
6			Nutrition report	5 days	Tue 21/07/20	Mon 27/07/24																	
7			Secure fruit suppliers	20 days	Tue 04/08/20	Mon 31/08/20	5,6																
8			Initial Production	85 days	Tue 21/07/20	Mon 16/11/20																	
9			Equipment rabab	30 days	Tue 21/07/20	Mon 31/08/20	4																
10			Production trials	15 days	Tue 01/09/20	Mon 21/09/27,9																	
11			Quality trials	20 days	Tue 22/09/20	Mon 19/10/210																	
12			Quality metrics	5 days	Tue 20/10/20	Mon 26/10/211																	
13			Quality training	15 days	Tue 27/10/20	Mon 16/11/212																	
14			Distribution	55 days	Tue 04/08/20	Mon 19/10/2																	
15			Market testing	30 days	Tue 04/08/20	Mon 14/09/25,6																	
16			Package design	15 days	Tue 15/09/20	Mon 05/10/215																	
17			Select distributor	25 days	Tue 15/09/20	Mon 19/10/27,15																	
18			Legal	15 days	Tue 15/09/20	Mon 05/10/2																	
21			Prepare product launch	15 days	Tue 17/11/20	Mon 07/12/20	13,16,17,19FS+25 days,20FS+15																

Project: Project Plan Part1

Date: Wed 03/06/20

Task

Split

Milestone

Summary

Project Summary

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

External Tasks

External Milestone

Deadline


Critical

Critical Split

Progress

Manual Progress

Slack

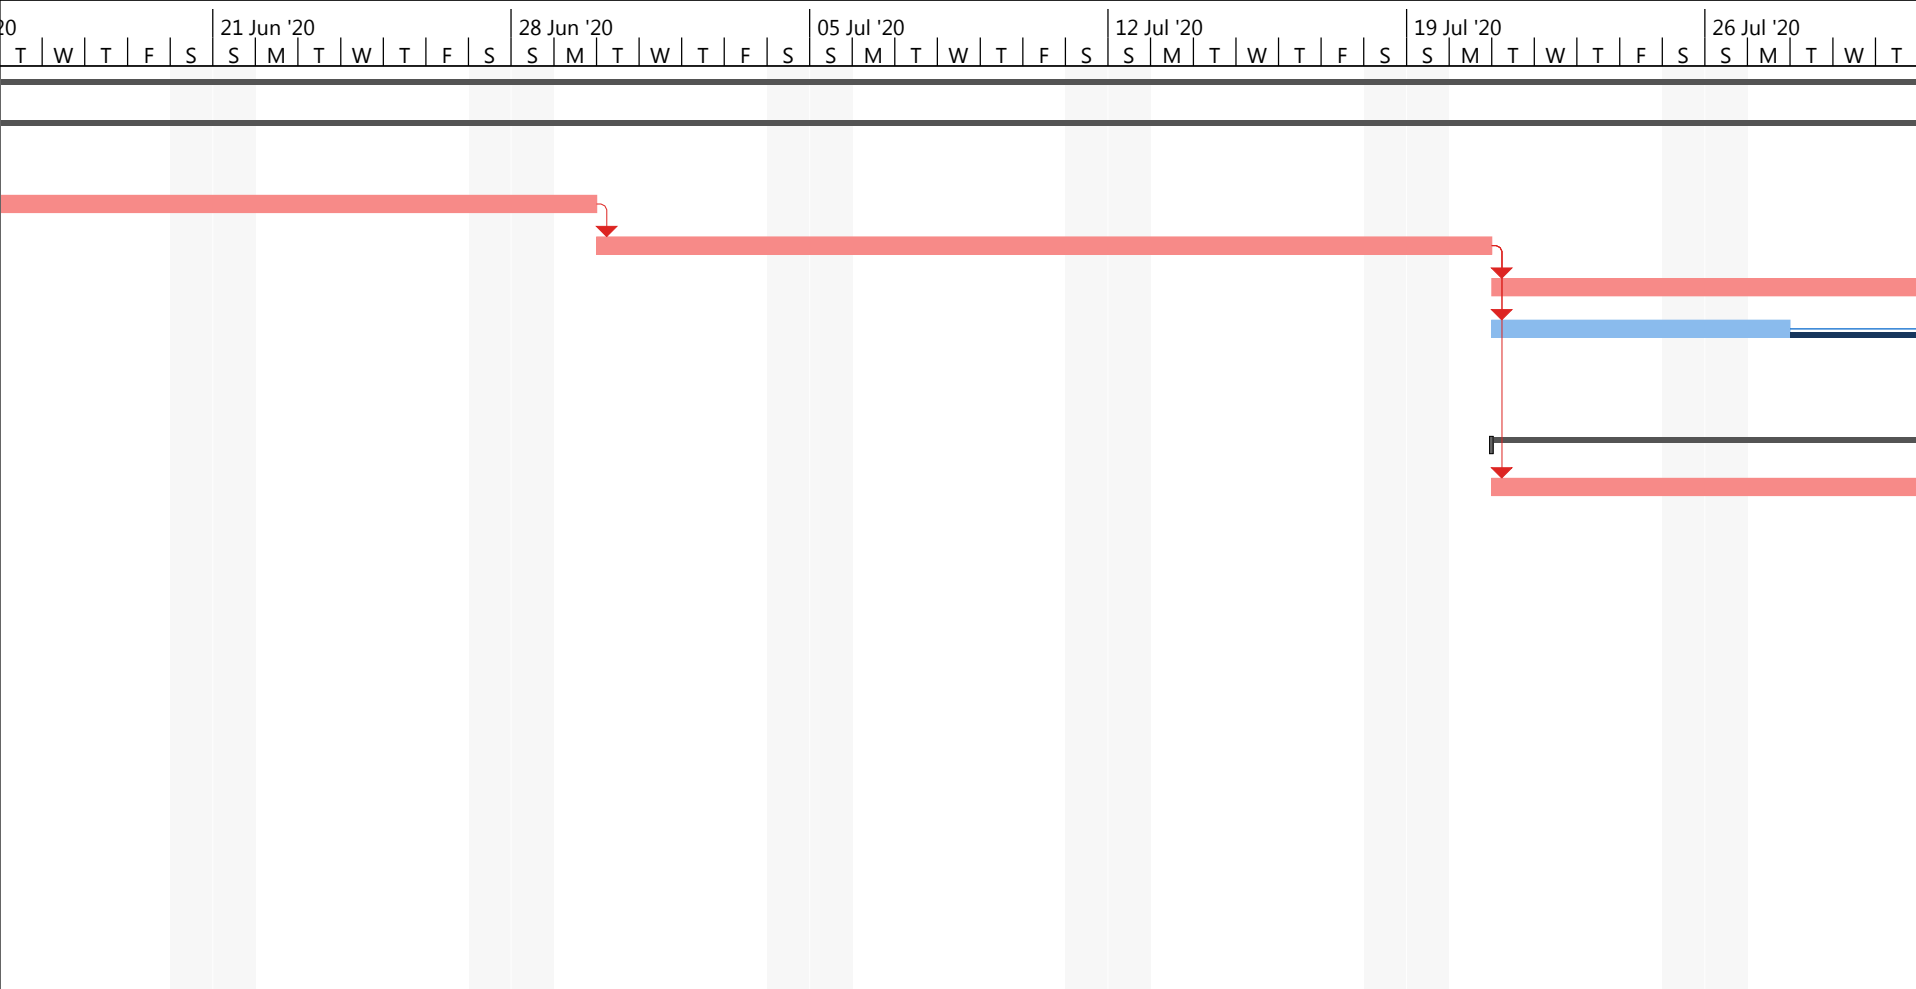

Project: Project Plan Part1
Date: Wed 03/06/20

Task		Manual Task		Deadline	
Split		Duration-only		Critical	
Milestone		Manual Summary Rollup		Critical Split	
Summary		Manual Summary		Progress	
Project Summary		Start-only		Manual Progress	
Inactive Task		Finish-only		Slack	
Inactive Milestone		External Tasks			
Inactive Summary		External Milestone			

