


Learning Team C Wk5 Rev A

ID		ES	EF	LS	LF	Task Mode	Task Name	Duration	Start	Finish	Qtr 1, 2012 Jan	Qtr 2, 2012 Feb	Qtr 3, 2012 Mar	Qtr 4, 2012 Apr	Qtr 1, 2012 May	Qtr 2, 2012 Jun	Qtr 3, 2012 Jul	Qtr 4, 2012 Aug	Qtr 1, 2012 Sep	Qtr 2, 2012 Oct	Qtr 3, 2012 Nov	Qtr 4, 2012 Dec	Qtr 1, 2012 Jan
1		0	1	0	1		1.0 POM+ Project																
2							1.1 R&D product development	55 days	Tue 1/3/12	Mon 3/19/12													
3		-1827	-1804	-1827	-1804		1.1.1 Need survey	23 days	Tue 1/3/12	Thu 2/2/12													
4		-1804	-1786	-1804	-1786		1.1.2 Set product specs	18 days	Fri 2/3/12	Tue 2/28/12													
5		-1786	-1776	-1786	-1776		1.1.3 Shelf life report	10 days	Wed 2/29/12	Tue 3/13/12													
6		-1776	-1772	-1776	-1772		1.1.4 Nutrition report	4 days	Wed 3/14/12	Mon 3/19/12													
7		-1772	-1752	-1772	-69		1.2 Secure fruit suppliers	20 days	Tue 3/20/12	Mon 4/16/12													
8							1.3 Initial Production	90 days	Wed 2/29/12	Tue 7/3/12													
9		-1786	-1751	-1786	-69		1.3.1 Equipment rehab	35 days	Wed 2/29/12	Tue 4/17/12													
10		-1751	-1736	-69	-54		1.3.2 Production trials	15 days	Wed 4/18/12	Tue 5/8/12													
11		-1736	-1716	-54	-34		1.3.3 Quality trials	20 days	Wed 5/9/12	Tue 6/5/12													
12		-1716	-1711	-34	-29		1.3.4 Quality metrics	5 days	Wed 6/6/12	Tue 6/12/12													
13		-1711	-1696	-29	-14		1.3.5 Quality training	15 days	Wed 6/13/12	Tue 7/3/12													
14							1.4 Distribution	85 days	Tue 3/20/12	Mon 7/16/12													
15		-1772	-1702	-99	-54		1.4.1 Market testing	30 days	Tue 4/24/12	Mon 6/25/12													
16		-1702	-1687	-29	-14		1.4.2 Package design	15 days	Tue 6/26/12	Mon 7/16/12													
17		-1772	-1747	-39	-14		1.4.3 Select distributors	25 days	Tue 3/20/12	Mon 4/23/12													
18							1.5 Legal	15 days	Tue 6/26/12	Mon 7/16/12													
19		-1702	-1687	-54	-39		1.5.1 Complete FDA certification	15 days	Tue 6/26/12	Mon 7/16/12													
20		-1702	-1697	-34	-29		1.5.2 Register trademark	5 days	Tue 6/26/12	Mon 7/2/12													
21		-1662	-1647	-14	1		1.6 Prepare product launch	15 days	Tue 8/21/12	Mon 9/10/12													

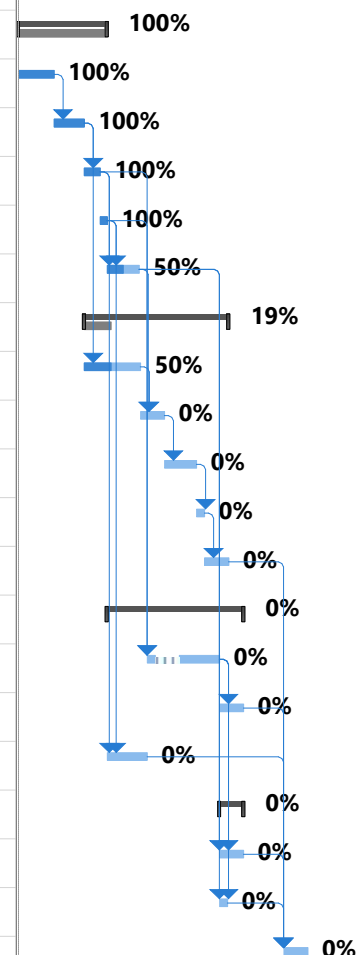

Critical		Manual Task		Baseline Milestone		External Tasks	
Critical Split		Start-only		Milestone		External Milestone	
Critical Progress		Finish-only		Summary Progress		Inactive Task	
Task		Duration-only		Summary		Inactive Milestone	
Split		Baseline		Manual Summary		Inactive Summary	
Task Progress		Baseline Split		Project Summary		Deadline	
